



Amherst Island Wind Project

ID	Task Name	% Complete	Duration	Start	Finish	Predecessors	2018											
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
1	Construction	0%	273 days	9/1/17	9/18/18		[Gantt bar from Sep 1, 2017 to Sep 18, 2018]											
2	EPC Construction Works	0%	317 days	9/1/17	9/18/18		[Gantt bar from Sep 1, 2017 to Sep 18, 2018]											
3	Civil Works	0%	317 days	9/1/17	9/18/18		[Gantt bar from Sep 1, 2017 to Sep 18, 2018]											
4	Mobilize to Island Site	0%	11 days	9/1/17	9/14/17		[Green bar from Sep 1, 2017 to Sep 14, 2017]											
5	Public Road Restoration	0%	193 days	9/11/17	9/18/18		[Gantt bar from Sep 11, 2017 to Sep 18, 2018]											
6	2nd Conc. Rd - (Stella 40' Rd to S31 Access)	0%	6 days	9/11/17	9/16/17	4SS+7 days	[Green bar from Sep 11, 2017 to Sep 16, 2017]											
7	Construction - Dump Road (Tower S31 Access)	0%	3 days	9/18/17	9/20/17	6	[Green bar from Sep 18, 2017 to Sep 20, 2017]											
8	2nd Conc. Rd - (S31/Dump Rd to S22 Access)	0%	4 days	9/21/17	9/25/17	7	[Green bar from Sep 21, 2017 to Sep 25, 2017]											
9	2nd Conc. Rd - (S22 Access to S04 Access)	0%	4 days	9/26/17	9/29/17	8	[Green bar from Sep 26, 2017 to Sep 29, 2017]											
10	2nd Conc. Rd - (S04 Access to S01/S29 Access)	0%	5 days	9/30/17	10/5/17	9	[Green bar from Sep 30, 2017 to Oct 5, 2017]											
11	Stella 40' RD - (2nd Conc. To 3rd Conc.)	0%	4 days	10/6/17	10/11/17	10	[Green bar from Oct 6, 2017 to Oct 11, 2017]											
12	Stella 40' RD - (3rd Conc. To S37 Access)	0%	4 days	10/12/17	10/16/17	11	[Green bar from Oct 12, 2017 to Oct 16, 2017]											
13	South Shore Rd. - (S02 Access to S14 Access)	0%	5 days	10/17/17	10/21/17	12	[Green bar from Oct 17, 2017 to Oct 21, 2017]											
14	South Shore Rd. - (S14 Access to S33 Access)	0%	13 days	10/23/17	11/8/17	13	[Green bar from Oct 23, 2017 to Nov 8, 2017]											
15	Lower 40' Rd.	0%	6 days	11/9/17	11/15/17	14	[Green bar from Nov 9, 2017 to Nov 15, 2017]											
16	Front Rd - (Marshal 40' Rd to Lower 40')	0%	8 days	11/16/17	11/24/17	15	[Green bar from Nov 16, 2017 to Nov 24, 2017]											
17	3rd Concession Rd	0%	14 days	11/25/17	12/11/17	16	[Green bar from Nov 25, 2017 to Dec 11, 2017]											
18	Post Construction Road Remediation - Sitewide	0%	13 days	9/4/18	9/18/18	17	[Green bar from Sep 4, 2018 to Sep 18, 2018]											
19	Access Road Construction	0%	64 days	9/14/17	11/28/17		[Gantt bar from Sep 14, 2017 to Nov 28, 2017]											
41	Island Transmission Lines	0%	103 days	10/2/17	2/2/18		[Gantt bar from Oct 2, 2017 to Feb 2, 2018]											
42	Transmission Line Installation	0%	88 days	10/2/17	1/16/18	4SS+25 day	[Green bar from Oct 2, 2017 to Jan 16, 2018]											
43	Transmission Line Testing and Commissioning	0%	15 days	1/17/18	2/2/18	42	[Green bar from Jan 17, 2018 to Feb 2, 2018]											
44	Collector System	0%	96 days	10/7/17	1/31/18		[Gantt bar from Oct 7, 2017 to Jan 31, 2018]											
45	Collector Circuit 1 - Trenching/Installation/Testing	0%	96 days	10/7/17	1/31/18		[Gantt bar from Oct 7, 2017 to Jan 31, 2018]											
46	Collector Line - S09 to junction JB105	0%	4 days	10/7/17	10/12/17	4SS,42SS+5	[Green bar from Oct 7, 2017 to Oct 12, 2017]											
47	Collector Line - S11 to junction JB105	0%	4 days	10/13/17	10/17/17	46	[Green bar from Oct 13, 2017 to Oct 17, 2017]											
48	Collector Line - Junction JB105 to S03	0%	1 day	10/18/17	10/18/17	47	[Green bar on Oct 18, 2017]											
49	Collector Line - S16 to junction JB105	0%	12 days	10/19/17	11/1/17	48	[Green bar from Oct 19, 2017 to Nov 1, 2017]											
50	Collector Line - S16 to junction JB104	0%	14 days	11/2/17	11/17/17	49	[Green bar from Nov 2, 2017 to Nov 17, 2017]											
51	Collector Line - S31 to junction JB104	0%	6 days	11/18/17	11/24/17	50	[Green bar from Nov 18, 2017 to Nov 24, 2017]											
52	Collector Line - S29 to S01	0%	5 days	11/25/17	11/30/17	51	[Green bar from Nov 25, 2017 to Nov 30, 2017]											


Project: Amherst Island Wind Project - Summary Scedule
Date: 7/24/17

Task Milestone Summary Project Summary Progress



Amherst Island Wind Project

ID	Task Name	% Complete	Duration	Start	Finish	Predecessors	2018															
							Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
53	Collector Line - S01 to junction JB101	0%	12 days	12/1/17	12/14/17	52																
54	Collector Line - S04 to junction JB101	0%	6 days	12/15/17	12/21/17	53																
55	Collector Line - Junction JB101 to junction JB 102	0%	6 days	12/22/17	12/30/17	54																
56	Collector Line - S22 to junction JB102	0%	5 days	1/2/18	1/6/18	55																
57	Collector Line - Junction JB102 to junction JB104	0%	7 days	1/8/18	1/15/18	56																
58	Collector Line - Junction JB104 to Substation	0%	12 days	1/16/18	1/29/18	57																
59	Collector Circuit #1 - Final Testing	0%	2 days	1/30/18	1/31/18	58																
60	Collector Circuit 2 - Trenching/Installation/Testing	0%	59 days	10/7/17	12/15/17																	
61	Collector Line - S36 to S21	0%	5 days	10/7/17	10/13/17	46SS																
62	Collector Line - S21 to S19	0%	4 days	10/14/17	10/18/17	61																
63	Collector Line - S19 to junction JB202	0%	2 days	10/19/17	10/20/17	62																
64	Collector Line - S02 to S27	0%	4 days	10/21/17	10/25/17	63																
65	Collector Line - S27 to S37	0%	3 days	10/26/17	10/28/17	64																
66	Collector Line - S37 to junction JB202	0%	1 day	10/30/17	10/30/17	65																
67	Collector Line - Junction JB202 to junction JB201	0%	13 days	10/31/17	11/14/17	66																
68	Collector Line - S05 - S20	0%	3 days	11/15/17	11/17/17	67																
69	Collector Line - S20 to S34	0%	5 days	11/18/17	11/23/17	68																
70	Collector Line - S34 to junction JB201	0%	11 days	11/24/17	12/6/17	69																
71	Collector Line - Junction JB201 to Substation	0%	5 days	12/7/17	12/13/17	70																
72	Collector Circuit #2 - Final Testing	0%	2 days	12/14/17	12/15/17	71																
73	Collector Circuit 3 - Trenching/Installation/Testing	0%	93 days	10/9/17	1/29/18																	
74	Collector line - S33 to S28	0%	3 days	10/9/17	10/11/17	61SS																
75	Collector line - S28 to S30	0%	23 days	10/12/17	11/7/17	61SS,74																
76	Collector line - S30 to S26	0%	5 days	11/8/17	11/13/17	75																
77	Collector line - S26 to S18	0%	4 days	11/14/17	11/17/17	76																
78	Collector line - S18 to S13	0%	3 days	11/17/17	11/21/17	77FS-1 day																
79	Collector line - S13 to junction JB301	0%	8 days	11/22/17	12/1/17	78																
80	Collector line - S07 to S14	0%	4 days	12/4/17	12/7/17	79																
81	Collector line - S14 to junction JB301	0%	6 days	12/8/17	12/15/17	80																
82	Collector line - Junction JB301 to Substation	0%	29 days	12/18/17	1/25/18	81																
83	Collector Circuit #3 - Final Testing	0%	2 days	1/26/18	1/29/18	82																

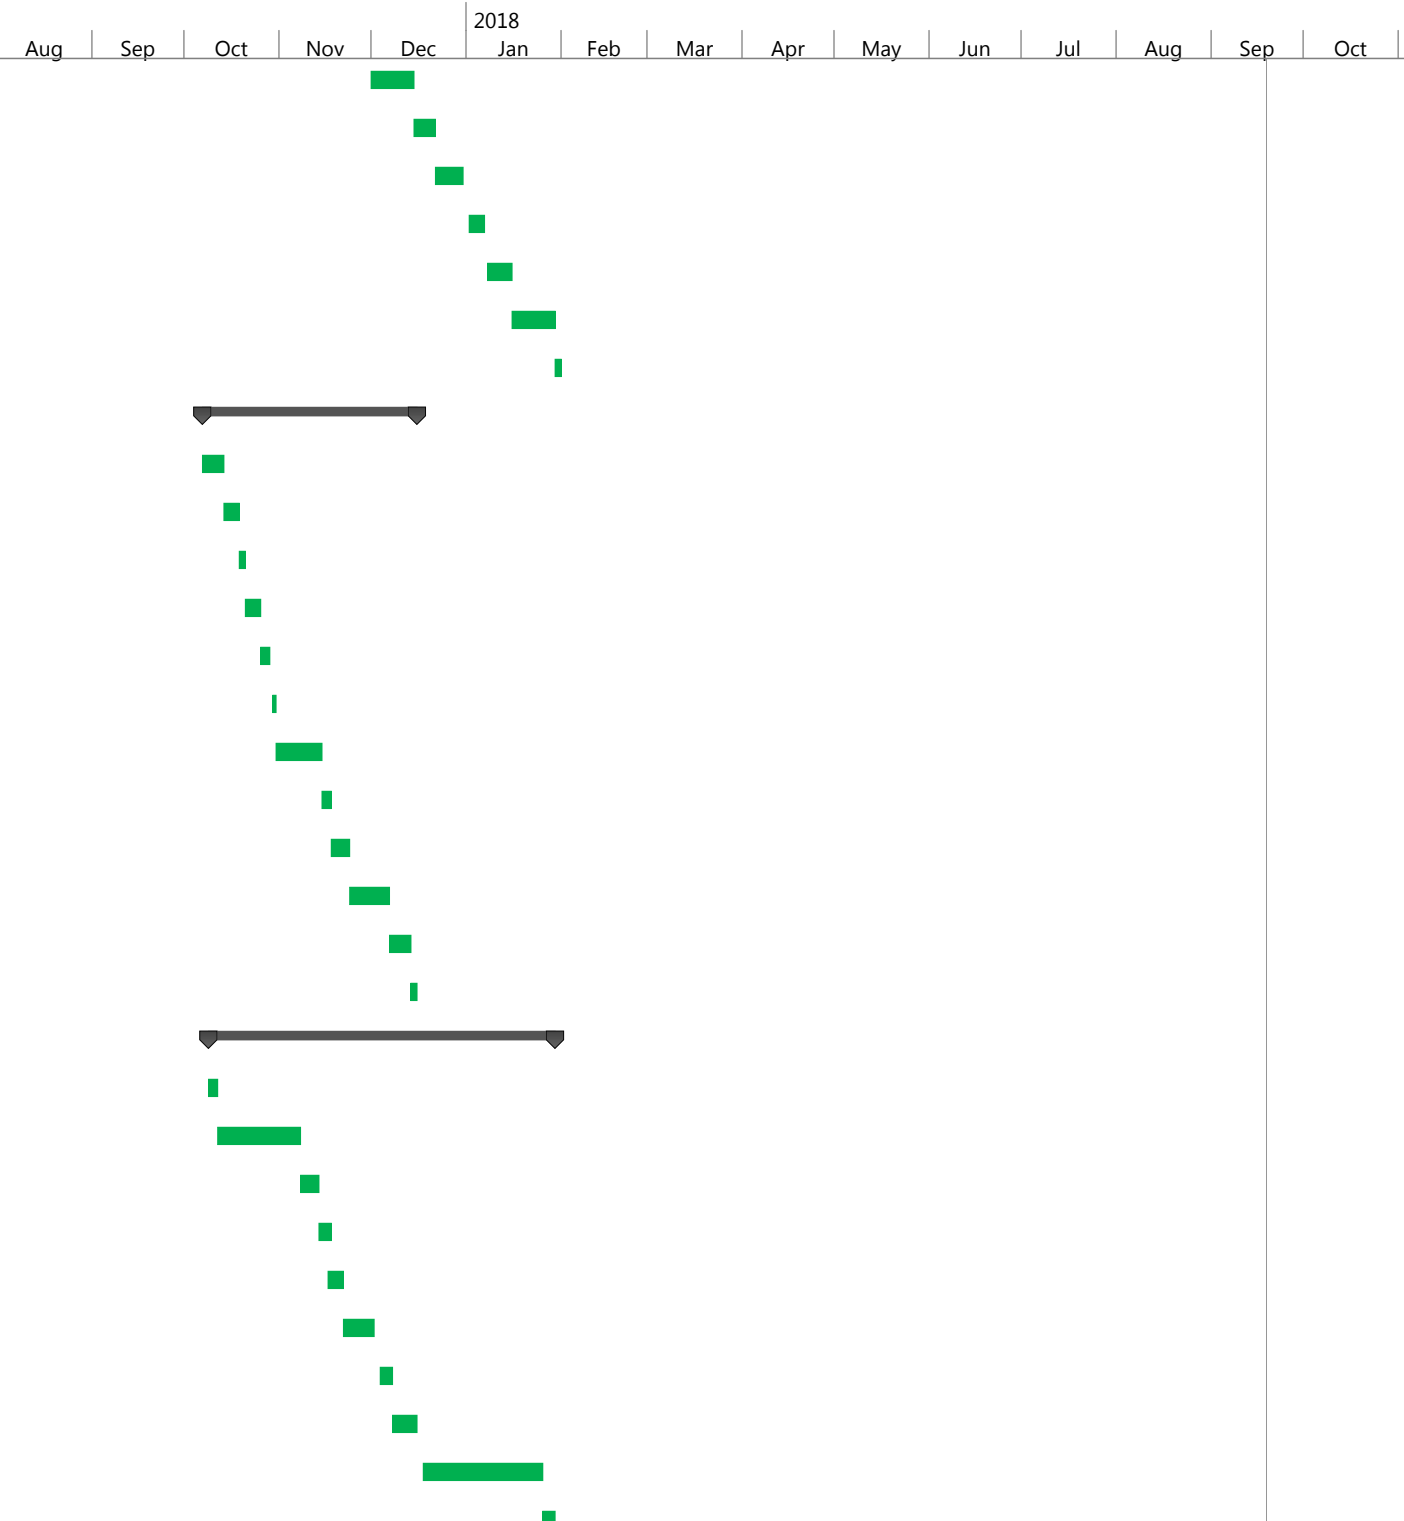

Project: Amherst Island Wind Project - Summary Scedule
 Date: 7/24/17

Task Milestone Summary Project Summary Progress
