


# Weekly Project Activity Map March 26th -31st

This map is for visual reference only and shows where project activity is anticipated to occur during the dates listed above. For daily updates please consult the project website ([amherstislandwindproject.com](http://amherstislandwindproject.com)), social media (Facebook and Twitter), or call 1-844-379-7740.

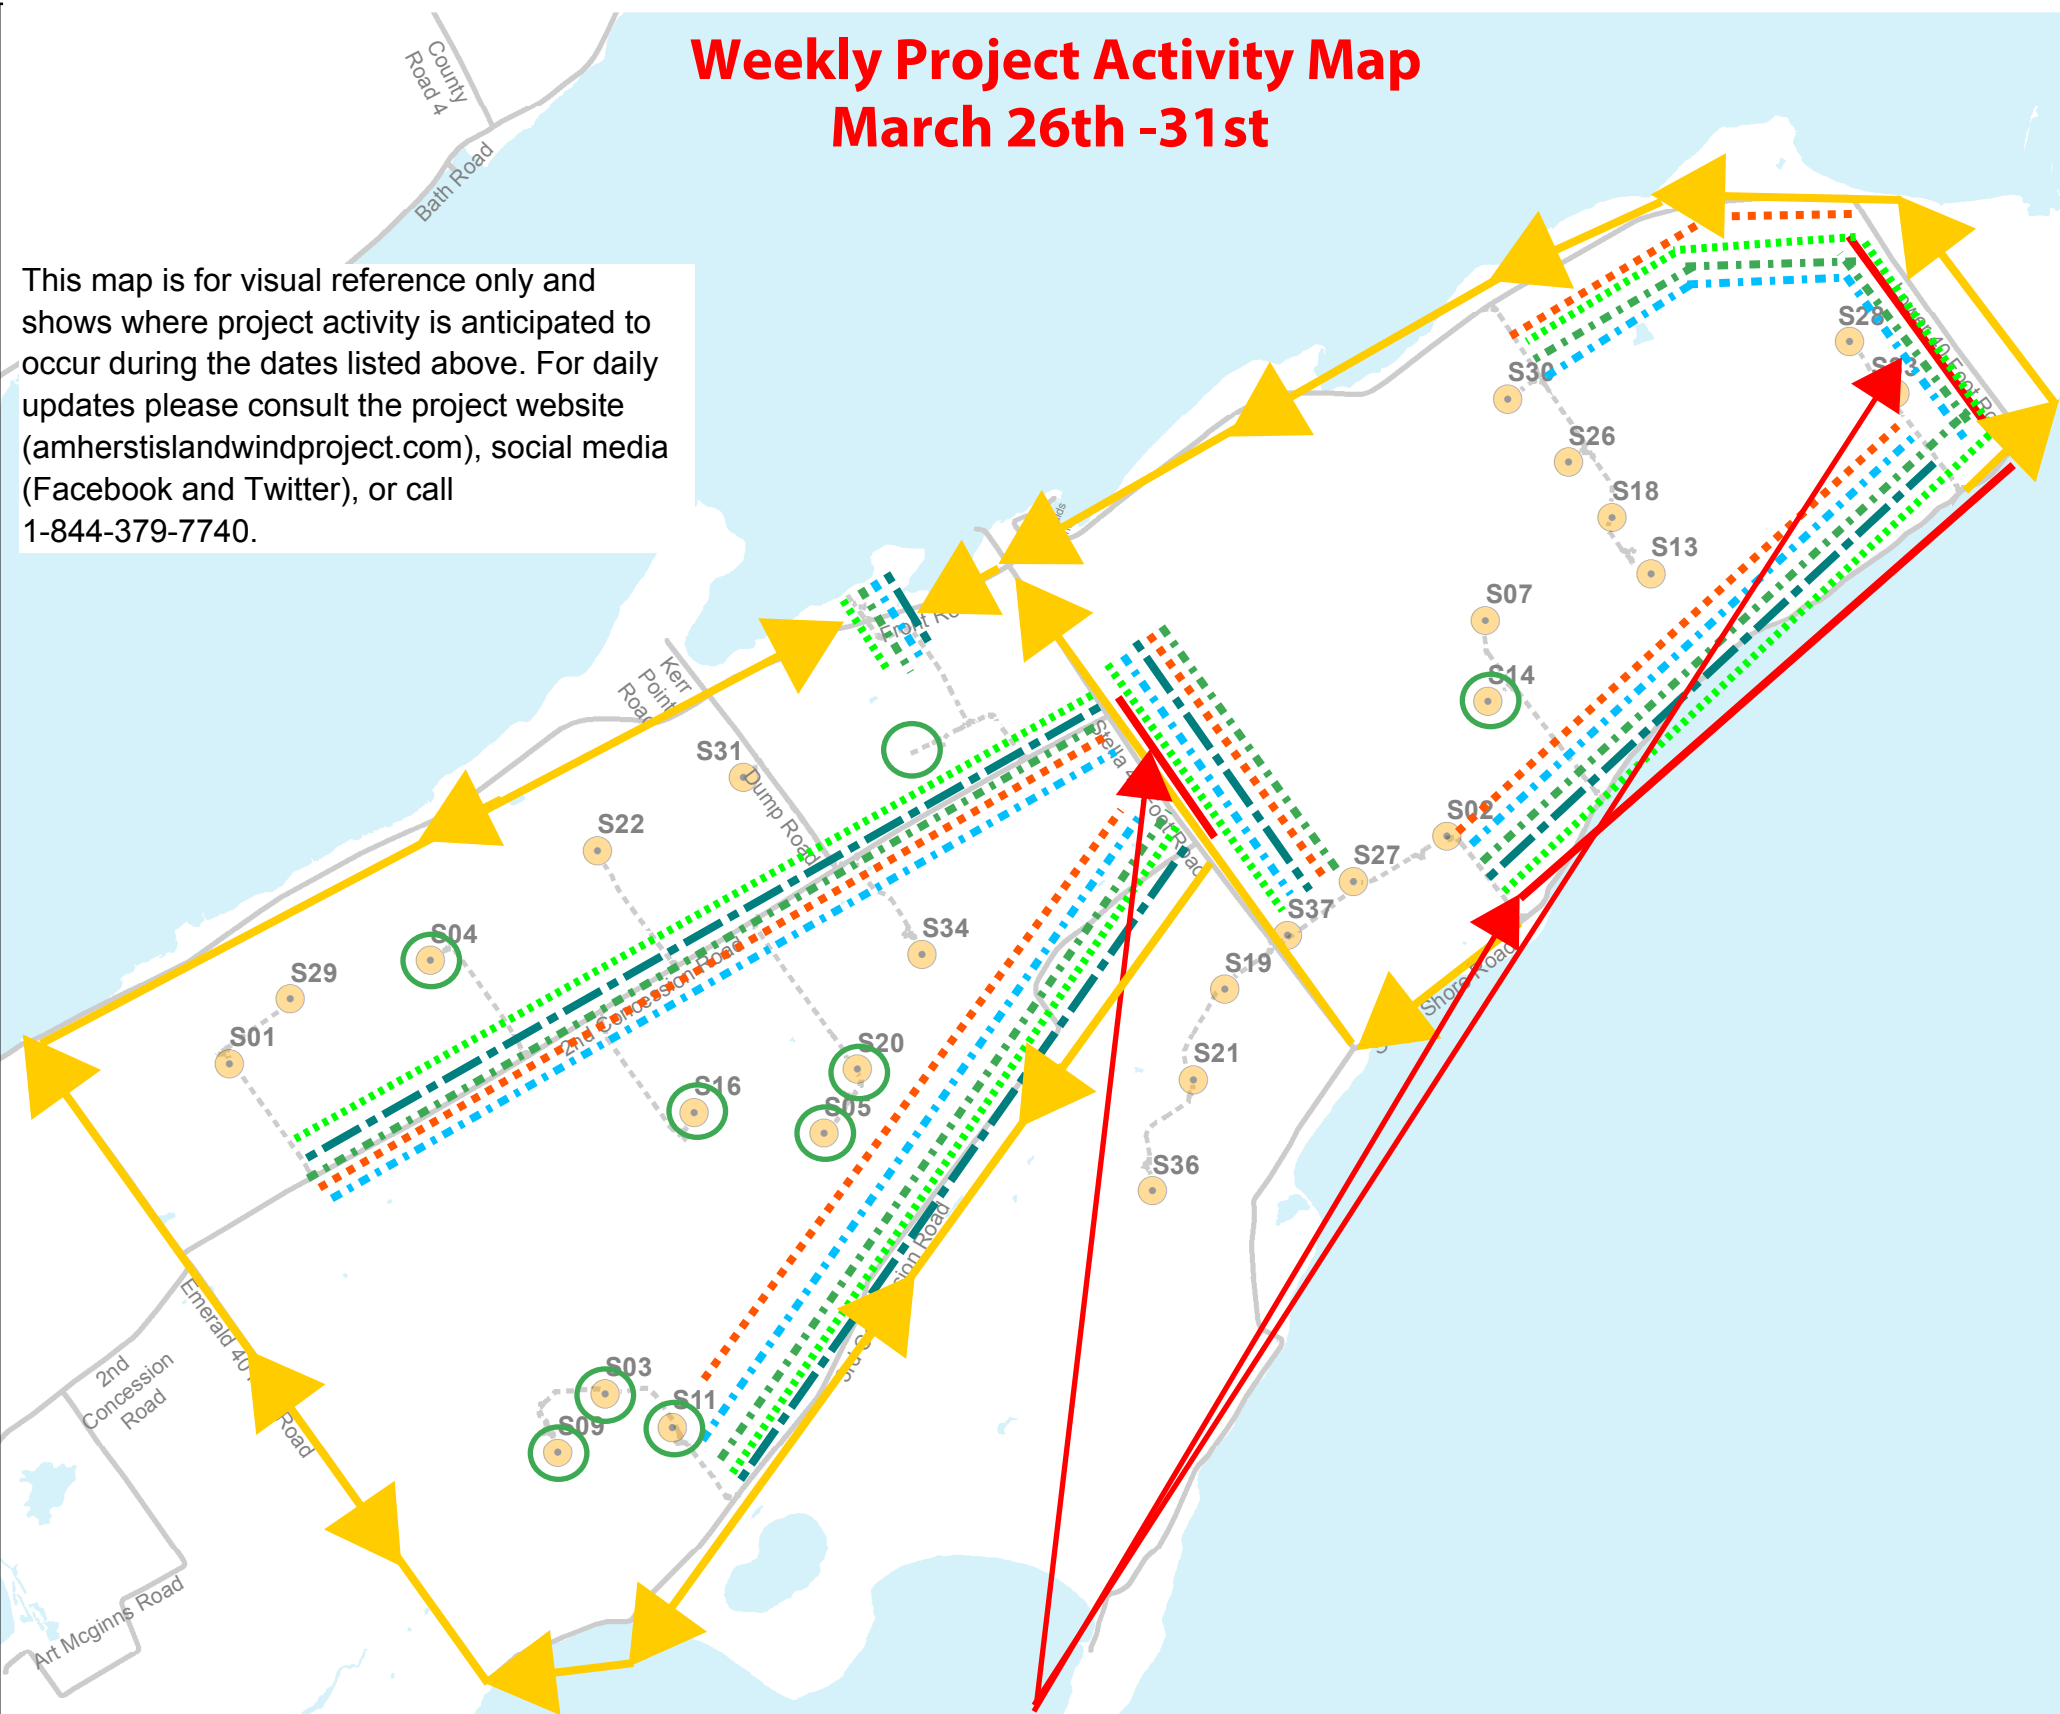

## Project Update

- Stella 40 Ft Rd will have a road closure on Monday, March 26th from 9:00 a.m. until 5:00 p.m. for municipal road upgrades. Detour routes will be posted.

- South Shore will have a road closure starting on Tuesday morning through to Thursday evening from Civic Address 4190 to 2300. Local traffic can access detour routes from the east and to the west. Once this work is completed Lower 40 Ft Road will close for municipal road upgrades.

- All road closures and detour routes will be conducted as per Rv.9 of the Windlectric Operations Plan.

## Noise By-law Exemption

Location	Reason for Exemption	Estimated Start Time	Estimated Completion Time
2 <sup>nd</sup> Concession 550	Foundation Preparation and Curing	Ongoing	ongoing
S04	Foundation Preparation and Curing	March 21 <sup>st</sup>	March 30 <sup>th</sup>
S16	Foundation Preparation and Curing	March 23 <sup>rd</sup>	April 9 <sup>th</sup>
S05	Foundation Preparation and Curing	March 25 <sup>th</sup>	April 2 <sup>nd</sup>
S20	Foundation Preparation and Curing	March 26 <sup>th</sup>	April 3 <sup>rd</sup>
S03	Foundation Preparation and Curing	March 22 <sup>nd</sup>	April 13 <sup>th</sup>
S11	Foundation Preparation and Curing	March 17 <sup>th</sup>	April 9 <sup>th</sup>
S09	Foundation Preparation and Curing	March 19 <sup>th</sup>	April 6 <sup>th</sup>
S14	Foundation Preparation and Curing	March 24 <sup>th</sup>	April 13 <sup>th</sup>

## Legend

- Turbine Locations
- Aggregate Delivery
- Single Lane Restrictions
- Existing Public Road
- Concrete Delivery
- Road Closures
- Project Access Road
- Component Delivery
- Detours
- Waterbodies
- Area of Potential Traffic Interruption
- Foundation Preparation and Curing
- Trenching



0 750 1,500  
Meters

**AMHERST ISLAND WIND PROJECT**

### Weekly Project Activity Map

DRAWING No. AMHST - 287      DATUM/PROJECTION: NAD83/UTM 18N
