


Revised - Weekly Project Activity Map April 23rd - April 28th

This map is for visual reference only and shows where project activity is anticipated to occur during the dates listed above. For daily updates please consult the project website (amherstislandwindproject.com), social media (Facebook and Twitter), or call 1-844-379-7740.

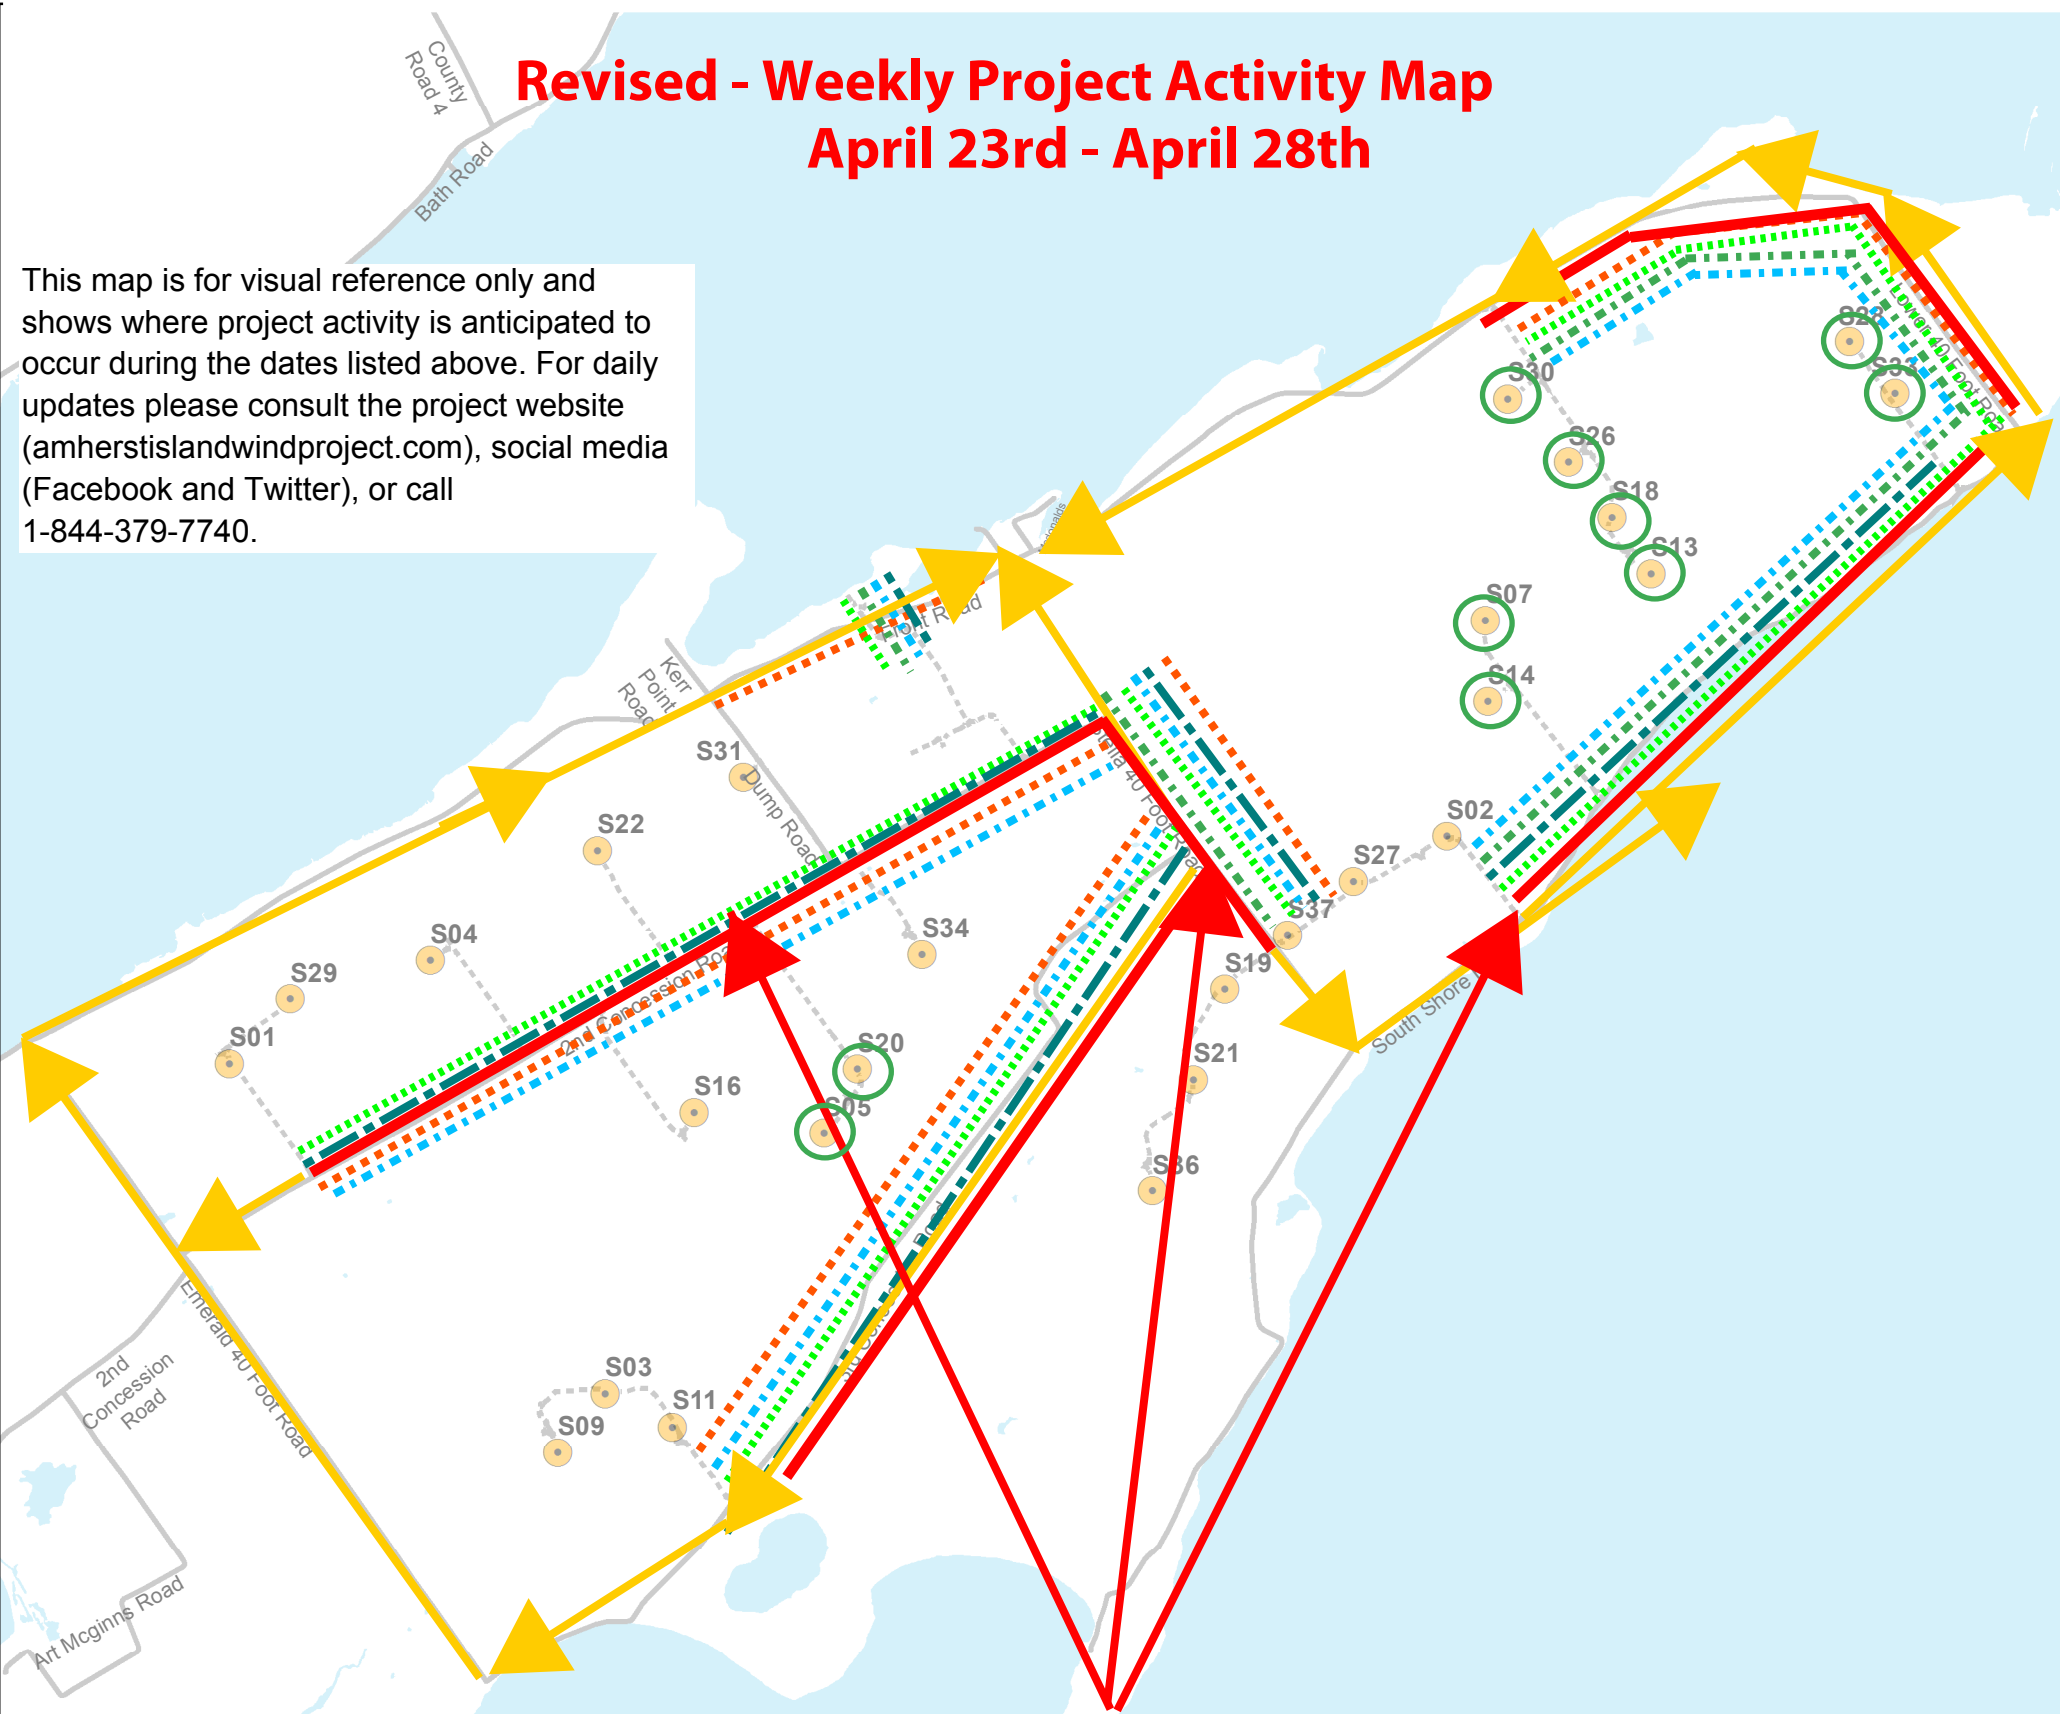

Project Update


- Stella 40 Ft Road will have a road closure for equipment and main erection crane relocation, component deliveries, collector installation and municipal road upgrades from Monday through Saturday from 2nd Concession to Civic Address 3040 and 3045
- 2nd Concession will have a road closure on Monday through Saturday for equipment and main erection crane relocation, component deliveries, collector installation and municipal road maintenance from Stella 40 Ft Rd to Civic Address 5440
- 3rd Concession will have a road closure on Monday through Saturday for equipment and main erection crane relocation, component deliveries, collector installation and municipal road maintenance from Stella 40 Ft Road to Civic Address 5000
- South Shore will have a road closure from Monday though Saturday from Civic Address 4190 to Civic Address 540
- Lower 40 Ft and Front Road from Civic Address 50 to 2375 will have an intermittent road closure from Tuesday to Saturday
- Some heavy loads will exceed 5000 kg per axle
- All other large transports, road closures and detour routes will be conducted as per Rv.9 of the Windlectric Operations Plan
- All updates will be posted nightly on the project website amherstislandwindproject.com

Noise By-law Exemption

Location	Reason for Exemption	Estimated Start Time	Estimated Completion Time
S33	Foundation Preparation and Curing	April 9 th	April 30 th
S28	Foundation Preparation and Curing	April 10 th	May 15 th
S07	Foundation Preparation and Curing	March 28 th	May 4 th
S14	Foundation Preparation and Curing	Feb 14 th	May 8 th
S20	Foundation Preparation and Curing	Feb 14 th	April 28 th
S05	Foundation Preparation and Curing	Feb 5 th	May 2 nd
S28	Foundation Preparation and Curing	April 19 th	May 15 th
S18	Foundation Preparation and Curing	April 30 th	May 24 th
S13	Foundation Preparation and Curing	May 3 rd	May 24 th
S30	Foundation Preparation and Curing	April 19 th	May 18 th

Legend

- Turbine Locations
- Existing Public Road
- Project Access Road
- Waterbodies
- Trenching
- Aggregate Delivery
- Concrete Delivery
- Component Delivery
- Area of Potential
- Traffic Interruption
- Single Lane Restrictions
- Road Closures
- Detours
- Foundation Preparation and Curing



AMHERST ISLAND WIND PROJECT

Weekly Project Activity Map

DRAWING No. AMHST - 287 DATUM/PROJECTION: NAD83/UTM 18N
