


Revised - Weekly Project Activity Map April 5th - April 7th

This map is for visual reference only and shows where project activity is anticipated to occur during the dates listed above. For daily updates please consult the project website (amherstislandwindproject.com), social media (Facebook and Twitter), or call 1-844-379-7740.

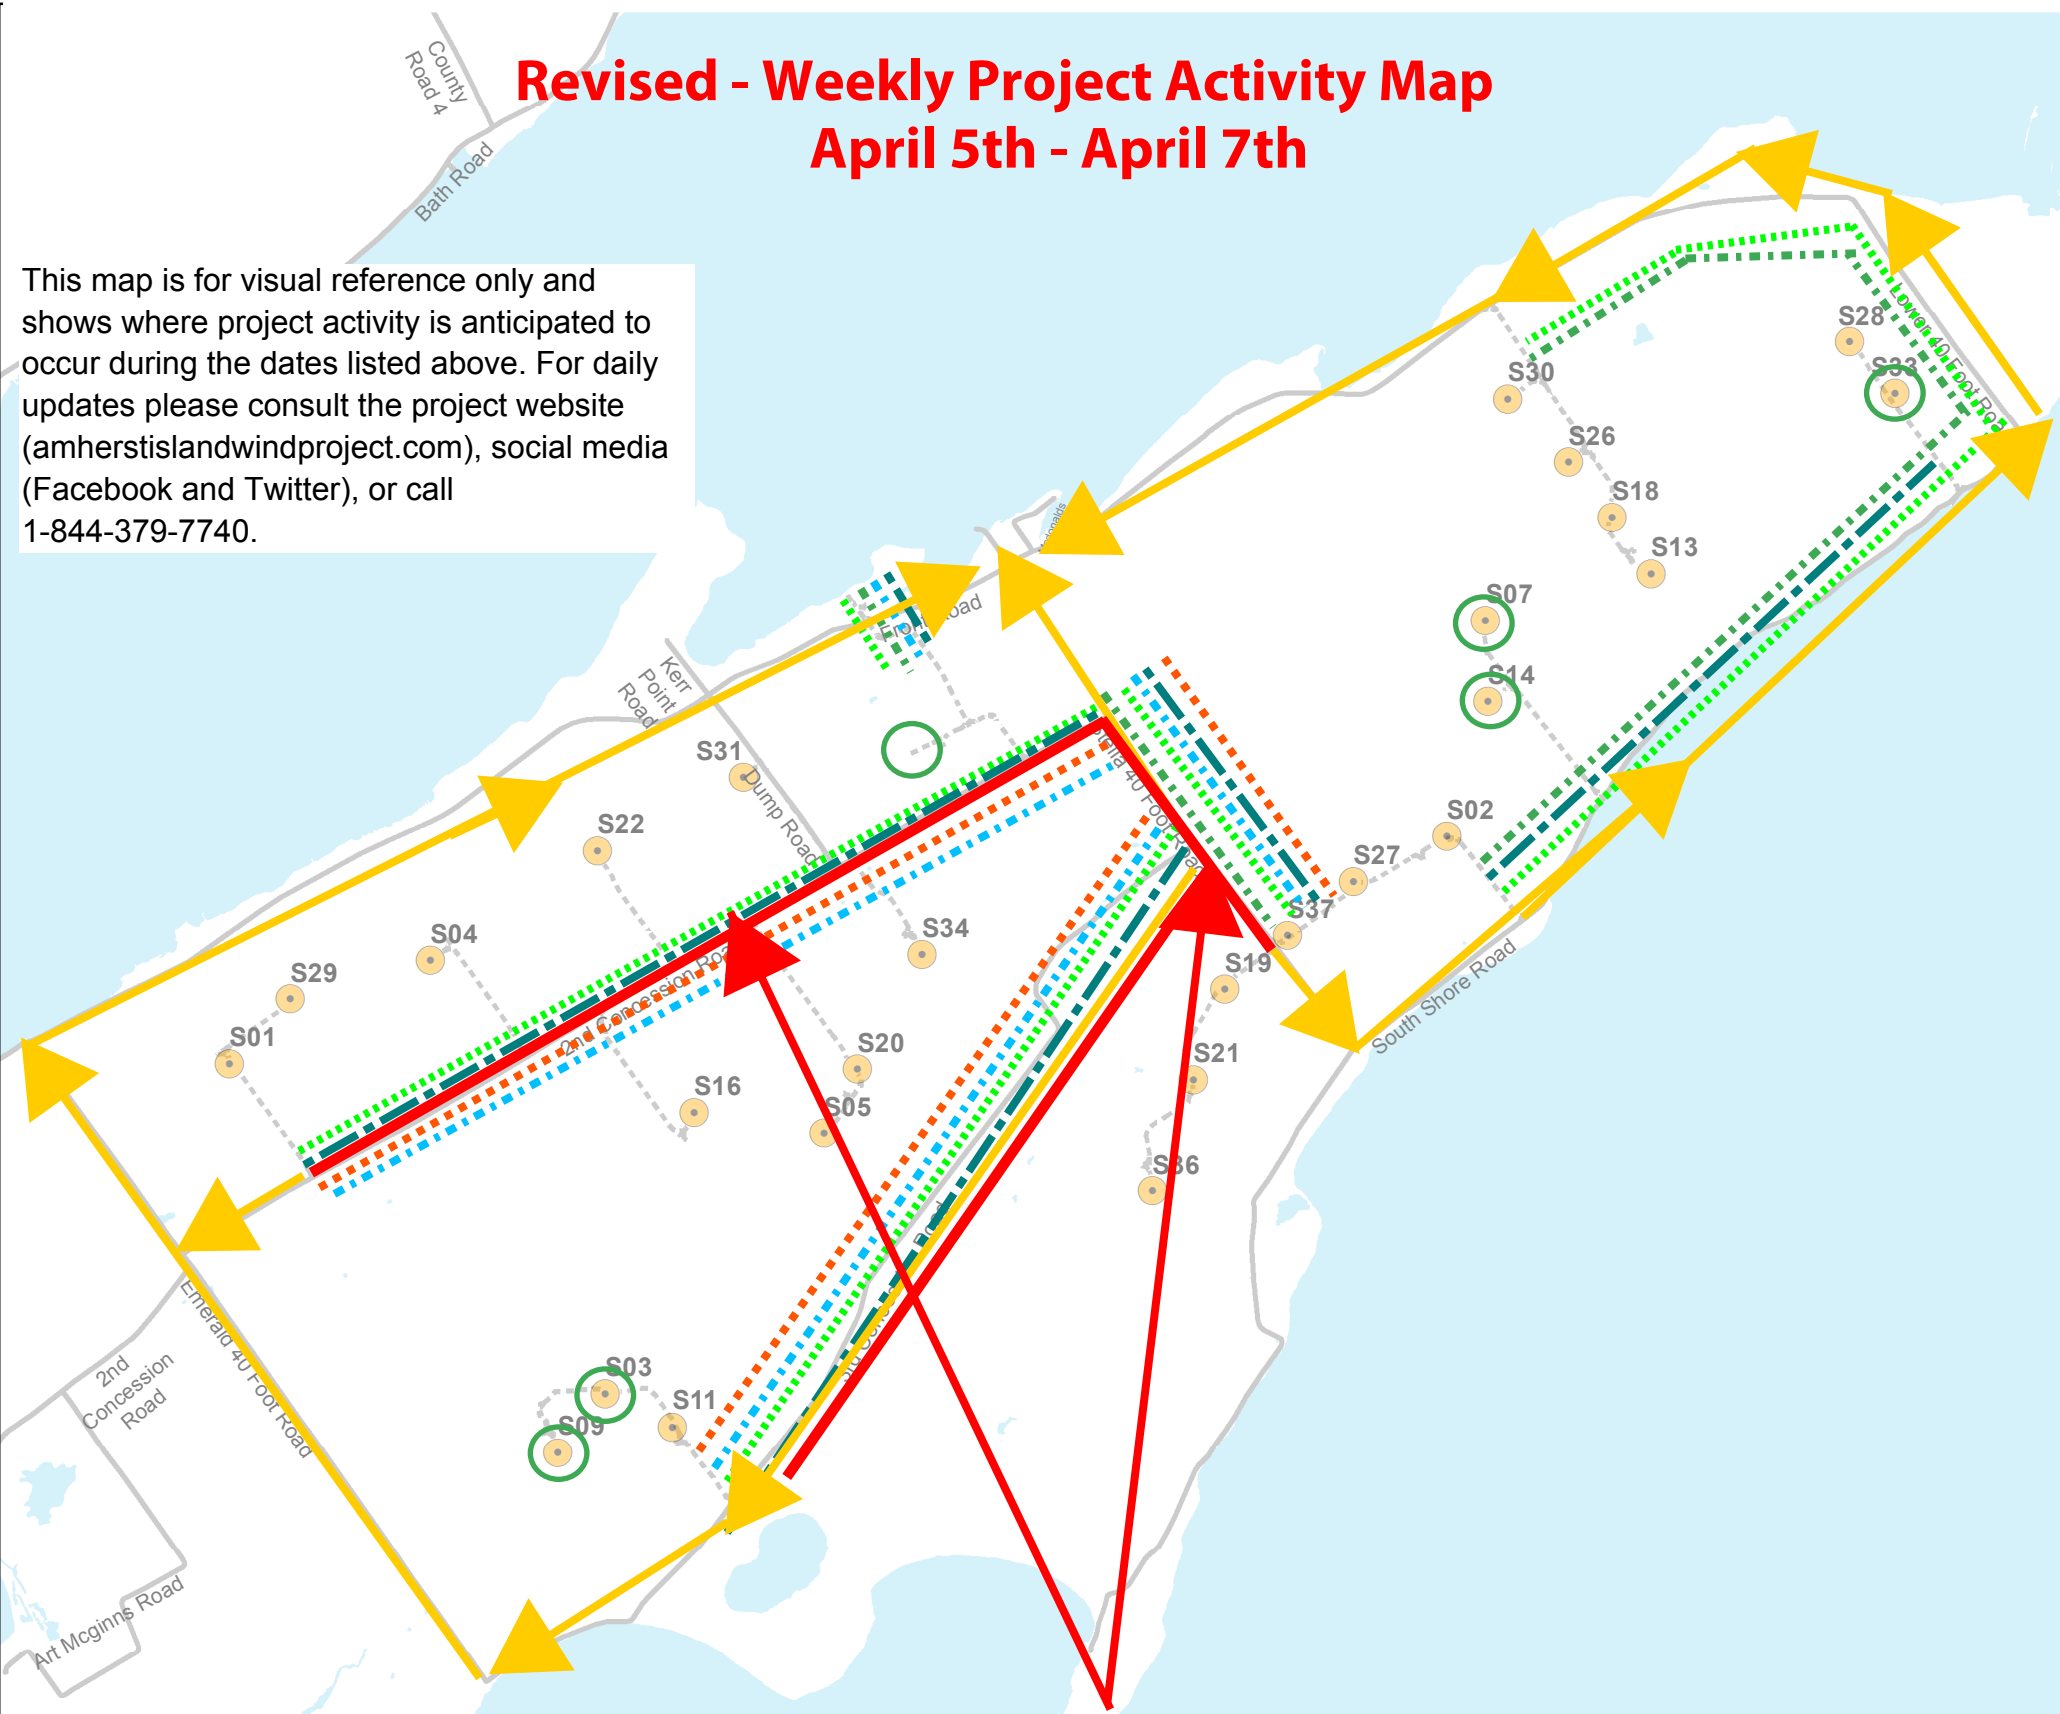

Project Update

- 2nd Concession will have a road closure for crane movement on Thursday, April 5th and Friday, April 6th. Immediately following the opening of 2nd Concession, 3rd Concession will close

-3rd Concession will have a road closure on Friday, April 6th and Saturday, April 7th for crane movement

- Stella 40 Ft Road will have a road closure on Thursday, April 5th, Friday, April 6th and Saturday, April 7th from 9:00 a.m. until 2.40 p.m. for crane movement

- All road closures and detour routes will be conducted as per Rv.9 of the Windlectric Operations Plan


- All updates will be posted nightly on the project website amherstislandwindproject.com

Noise By-law Exemption

Location	Reason for Exemption	Estimated Start Time	Estimated Completion Time
2nd Concession 550	Transformer Fill	Ongoing	ongoing
S33	Foundation Preparation and Curing	April 4 th	April 11 th
S03	Foundation Preparation and Curing	March 26 nd	April 13 th
S09	Foundation Preparation and Curing	March 19 th	April 6 th
S07	Foundation Preparation and Curing	March 30 th	April 9 th
S14	Foundation Preparation and Curing	March 24 th	April 13 th

Legend

- Turbine Locations
- ⋯ Aggregate Delivery
- ⋯ Single Lane Restrictions
- Existing Public Road
- - - Concrete Delivery
- Road Closures
- - - Project Access Road
- - - Component Delivery
- Detours
- Waterbodies
- - - Area of Potential
- Foundation Preparation and Curing
- Trenching
- ⋯ Traffic Interruption



AMHERST ISLAND WIND PROJECT

Weekly Project Activity Map

DRAWING No. AMHST - 287 DATUM/PROJECTION: NAD83/UTM 18N
