


Weekly Project Activity Map May 2nd - May 15th

This map is for visual reference only and shows where project activity is anticipated to occur during the dates listed above. For daily updates please consult the project website (amherstislandwindproject.com), social media (Facebook and Twitter), or call 1-844-379-7740.

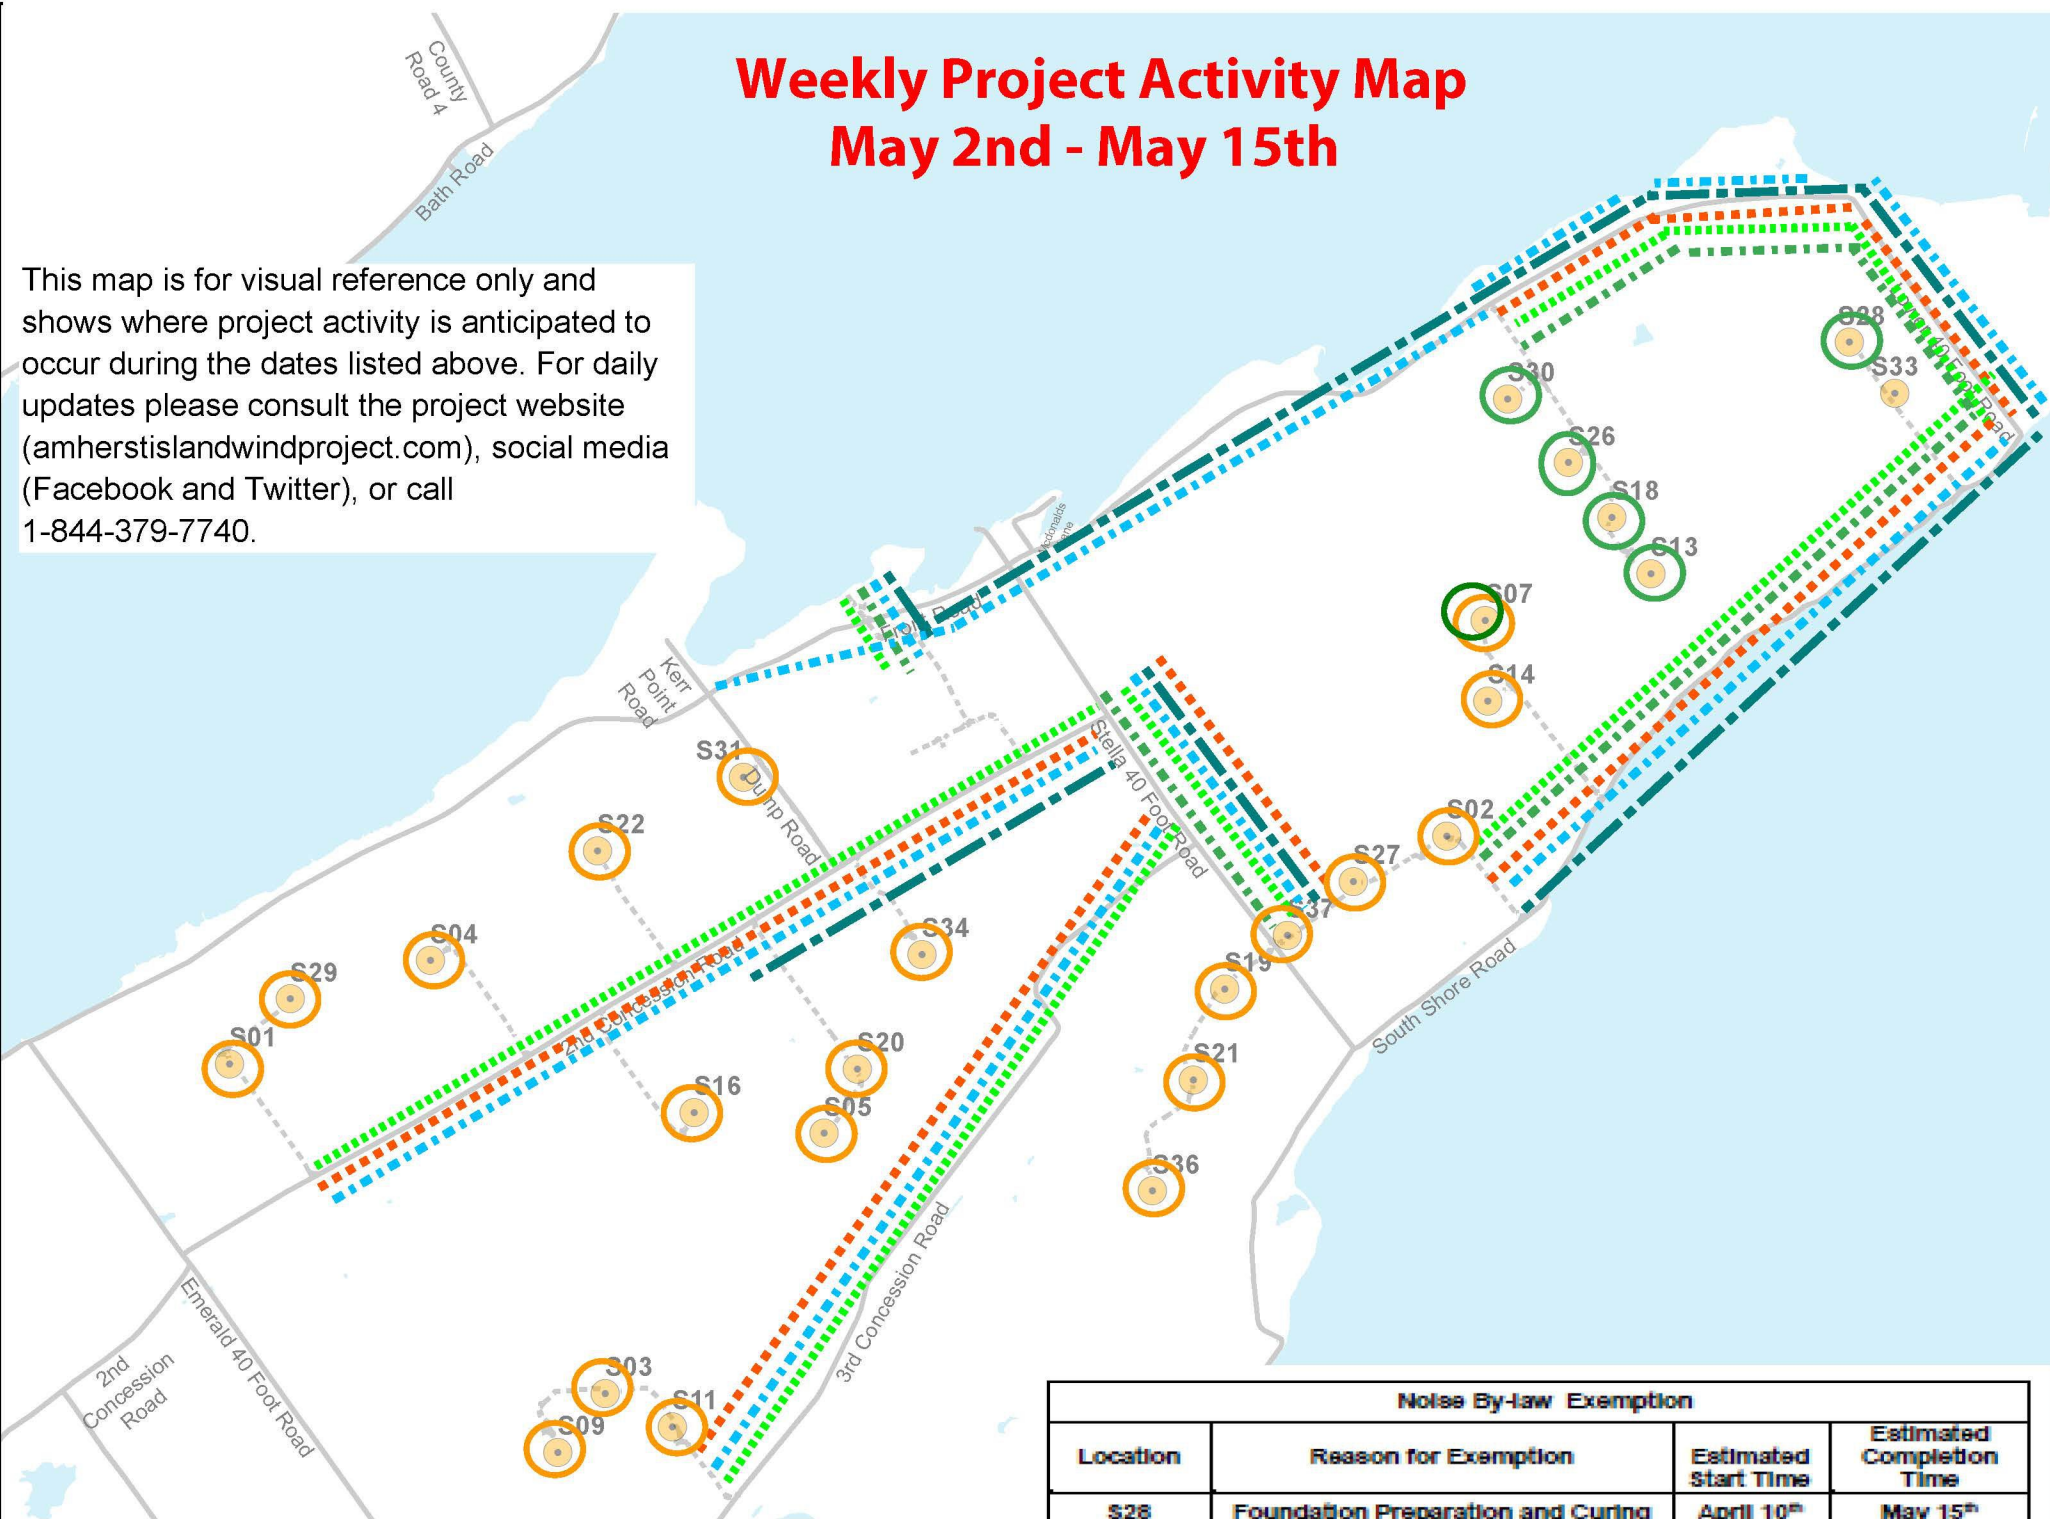

Project Update

- Stella 40 Ft Road will have construction traffic, component deliveries and municipal road maintenance from 2nd Concession to civic address 3040 and 3045
 - 2nd Concession will have construction traffic, component deliveries, collector installation and municipal road maintenance from Stella 40 Ft Rd to civic address 5440
 - 3rd Concession will have municipal road maintenance from Stella 40 Ft Road to civic address 5000
 - South Shore will have municipal road maintenance, construction traffic and component deliverers.
 - Front Road may have component deliveries from civic address 6605 to 2375 on May 8th and 10th and 14th from 11:00 am. - 2:20 p.m. and 3:30 p.m. to 7:00 p.m. There will be a traffic interruption in the area of civic address 6610 and 6605 while components move onto Front Road.
- Please note: In the event of weather delays, the deliveries will move to the next day (May 9th, May 11th and 15th) during the times listed above. If this occurs we will post a notice by 6:00 p.m. on the website and at the store the evening before.
- All road closures and detour routes will be conducted as per Rv.9 of the Windlectric Operations Plan
 - All updates will be posted nightly on the project website amherstislandwindproject.com

Noise By-law Exemption

Location	Reason for Exemption	Estimated Start Time	Estimated Completion Time
S28	Foundation Preparation and Curing	April 10 th	May 15 th
S07	Foundation Preparation and Curing	March 28 th	May 24 th
S26	Foundation Preparation and Curing	April 19 th	May 20 th
S18	Foundation Preparation and Curing	April 30 th	May 24 th
S16	Foundation Preparation and Curing	April 26 th	May 15 th
S13	Foundation Preparation and Curing	May 3 rd	May 24 th
S30	Foundation Preparation and Curing	April 19 th	May 18 th
S11	Night Shift Electrical Commissioning	May 1 st	May 11 th
S09	Night Shift Electrical Commissioning	May 1 st	May 11 th
S03	Night Shift Electrical Commissioning	May 2 nd	May 12 th
S05	Night Shift Electrical Commissioning	May 2 nd	May 12 th
S20	Night Shift Electrical Commissioning	May 2 nd	May 12 th
S31	Night Shift Electrical Commissioning	May 3 rd	May 18 th
S21	Night Shift Electrical Commissioning	May 4 th	May 19 th
S19	Night Shift Electrical Commissioning	May 5 th	May 19 th
S36	Night Shift Electrical Commissioning	May 3 rd	May 18 th
S37	Night Shift Electrical Commissioning	May 4 th	May 19 th
S27	Night Shift Electrical Commissioning	May 6 th	May 21 st
S02	Night Shift Electrical Commissioning	May 7 th	May 21 st
S04	Night Shift Electrical Commissioning	May 3 rd	May 18 th
S22	Night Shift Electrical Commissioning	May 5 th	May 21 st
S01	Night Shift Electrical Commissioning	May 7 th	May 21 st
S29	Night Shift Electrical Commissioning	May 8 th	May 22 nd
S07	Night Shift Electrical Commissioning	May 10 th	May 24 th
S14	Night Shift Electrical Commissioning	May 5 th	May 19 th
S34	Night Shift Electrical Commissioning	May 4 th	May 18 th

Legend

- Turbine Locations
- Aggregate Delivery
- Single Lane Restrictions
- Existing Public Road
- Concrete Delivery
- Road Closures
- Project Access Road
- Component Delivery
- Detours
- Foundation Preparation and Curing
- Waterbodies
- Area of Potential Traffic Interruption
- Trenching
- Electrical Commissioning



0 750 1,500
Meters

PENNECON
LIMITED

AMHERST ISLAND WIND PROJECT

Weekly Project Activity Map

DRAWING No. AMHST - 287

DATUM/PROJECTION: NAD83/UTM 18N
