


Weekly Project Activity Map May 2nd - May 15th

This map is for visual reference only and shows where project activity is anticipated to occur during the dates listed above. For daily updates please consult the project website (amherstislandwindproject.com), social media (Facebook and Twitter), or call 1-844-379-7740.

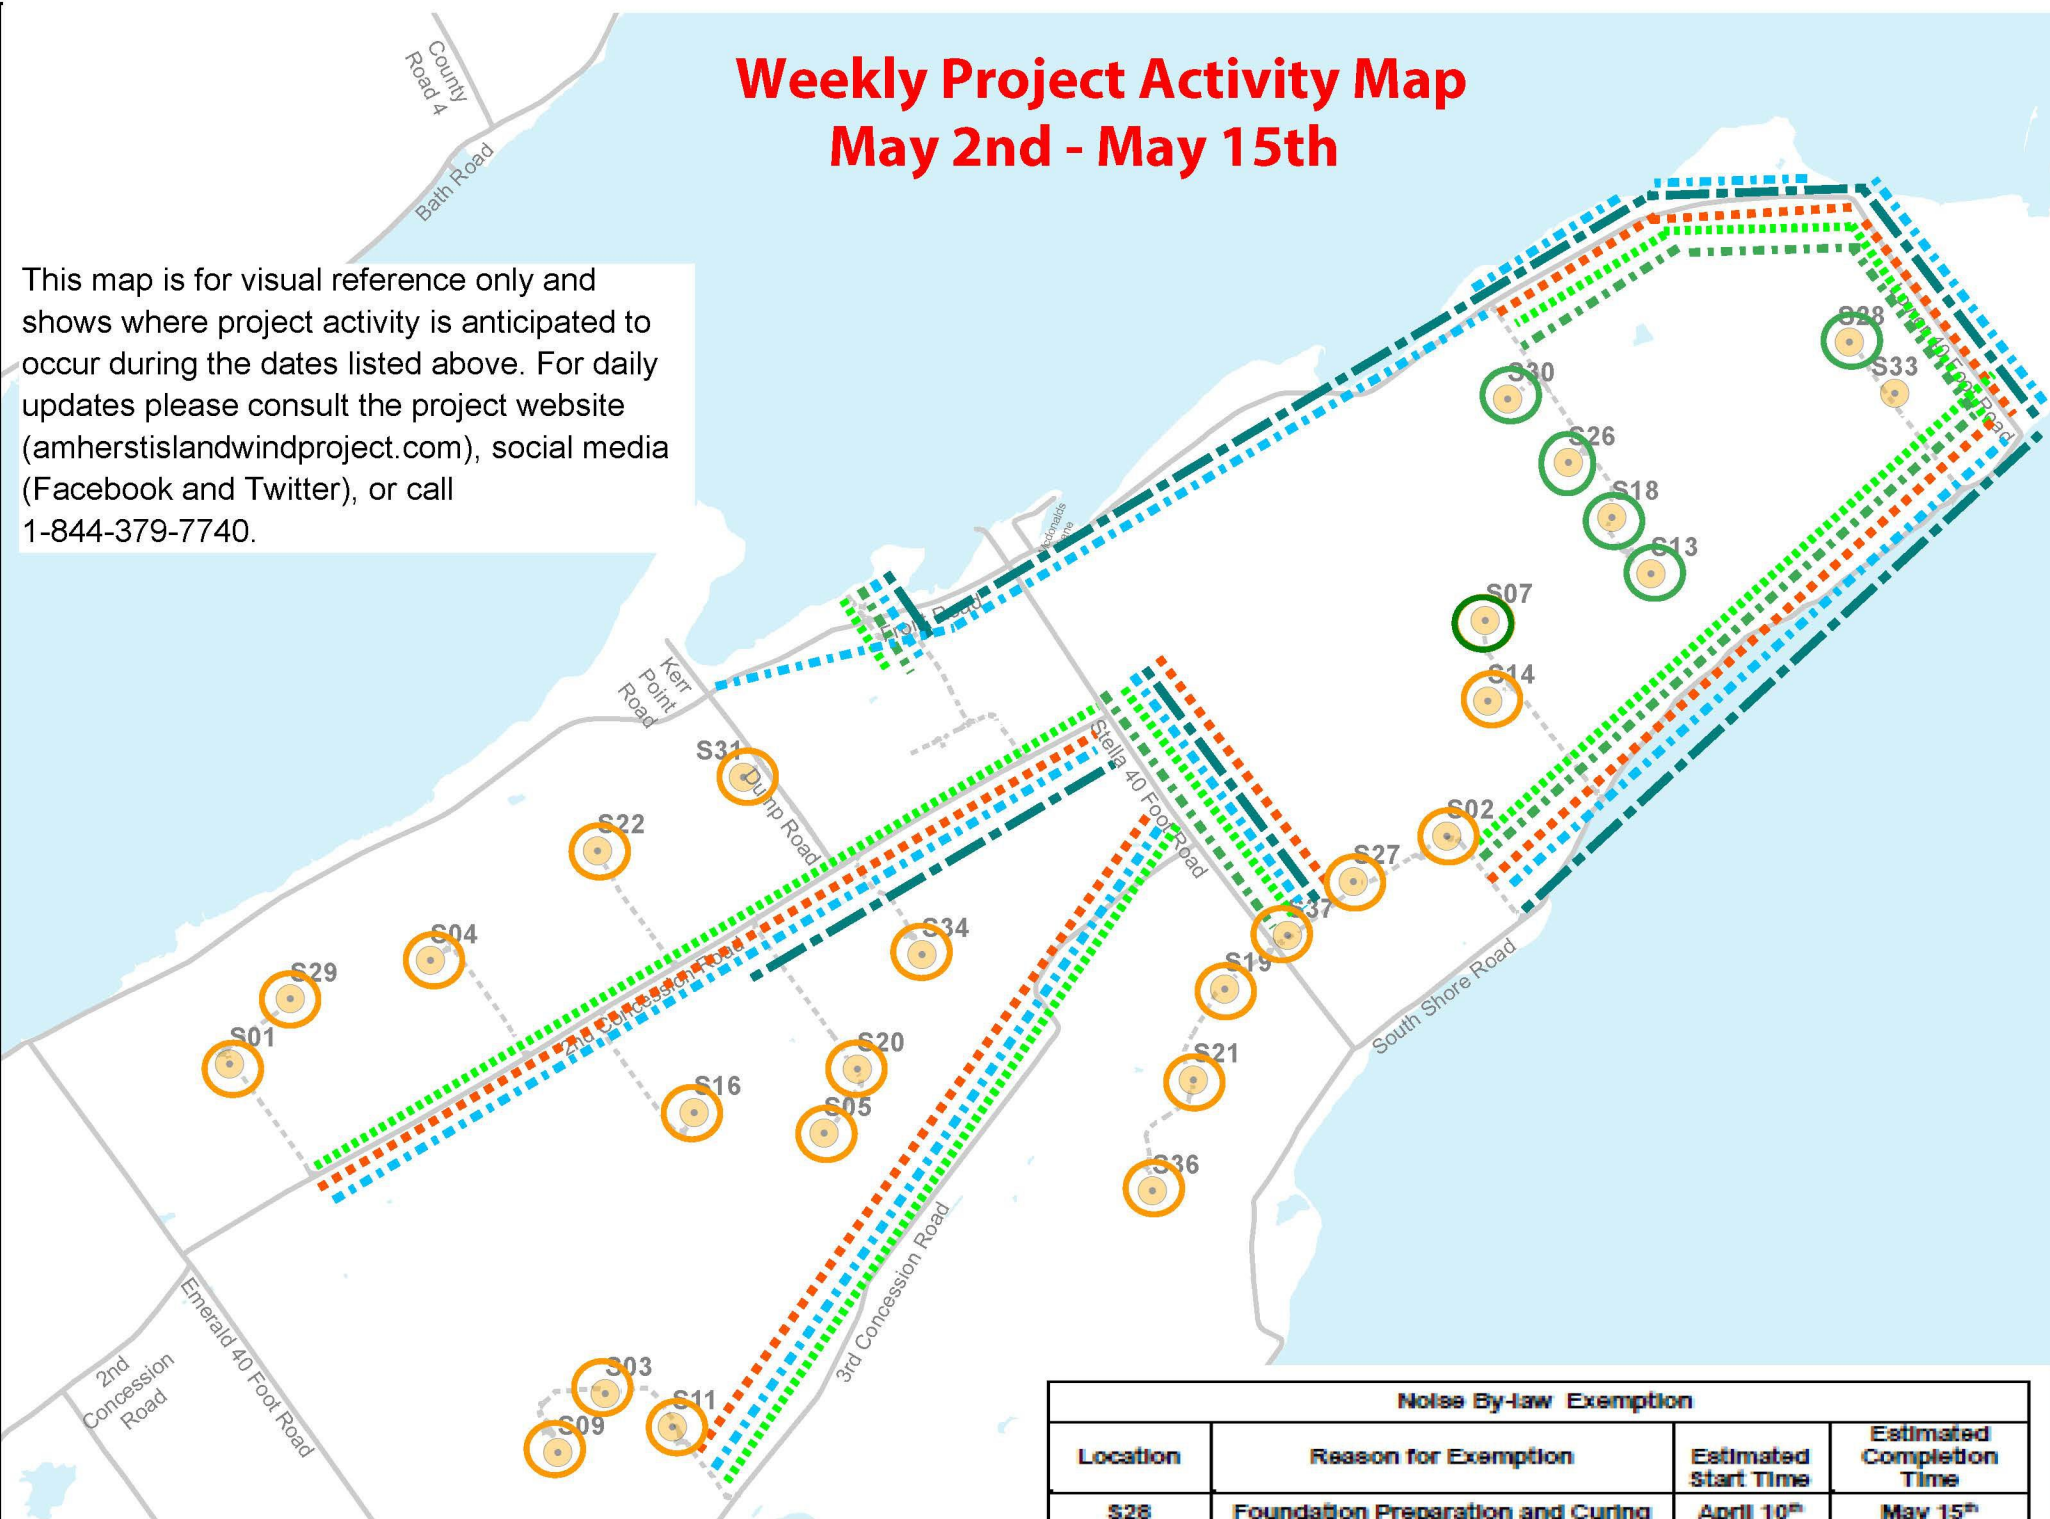

Project Update

- Stella 40 Ft Road will have construction traffic, component deliveries and municipal road maintenance from 2nd Concession to Civic Address 3040 and 3045
- 2nd Concession will have construction traffic, component deliveries, collector installation and municipal road maintenance from Stella 40 Ft Rd to Civic Address 5440
- 3rd Concession will have municipal road maintenance from Stella 40 Ft Road to Civic Address 5000
- South Shore will have municipal road maintenance a road closure daily from 9 - 12:00 p.m. for component deliveries
- Front Road may have component deliveries from Civic Address 6605 to 2375 on May 8th and 10th and 14th from 11:00 am. - 2:20 p.m. and 3:30 p.m. to 7:00 p.m. There will be a traffic interruption in the area of Civic address 6610 and 6605 while components move onto Front Road.

Please note: In the event of weather delays, the deliveries will move to the next day (May 9th, May 11th and 15th) during the times listed above. If this occurs we will post a notice by 6:00 p.m. on the website and at the store the evening before.

- All road closures and detour routes will be conducted as per Rv.9 of the Windlectric Operations Plan
- All updates will be posted nightly on the project website amherstislandwindproject.com

Noise By-law Exemption			
Location	Reason for Exemption	Estimated Start Time	Estimated Completion Time
\$28	Foundation Preparation and Curing	April 10 th	May 15 th
\$07	Foundation Preparation and Curing	March 28 th	May 24 th
\$26	Foundation Preparation and Curing	April 19 th	May 20 th
\$18	Foundation Preparation and Curing	April 30 th	May 24 th
\$16	Foundation Preparation and Curing	April 26 th	May 15 th
\$13	Foundation Preparation and Curing	May 3 rd	May 24 th
\$30	Foundation Preparation and Curing	April 19 th	May 18 th
\$11	Night Shift Electrical Commissioning	May 1 st	May 11 th
\$09	Night Shift Electrical Commissioning	May 1 st	May 11 th
\$03	Night Shift Electrical Commissioning	May 2 nd	May 12 th
\$05	Night Shift Electrical Commissioning	May 2 nd	May 12 th
\$20	Night Shift Electrical Commissioning	May 2 nd	May 12 th
\$31	Night Shift Electrical Commissioning	May 3 rd	May 18 th
\$21	Night Shift Electrical Commissioning	May 4 th	May 19 th
\$19	Night Shift Electrical Commissioning	May 5 th	May 19 th
\$36	Night Shift Electrical Commissioning	May 3 rd	May 18 th
\$37	Night Shift Electrical Commissioning	May 4 th	May 19 th
\$27	Night Shift Electrical Commissioning	May 6 th	May 21 st
\$02	Night Shift Electrical Commissioning	May 7 th	May 21 st
\$04	Night Shift Electrical Commissioning	May 3 rd	May 18 th
\$22	Night Shift Electrical Commissioning	May 5 th	May 21 st
\$01	Night Shift Electrical Commissioning	May 7 th	May 21 st
\$29	Night Shift Electrical Commissioning	May 8 th	May 22 nd
\$07	Night Shift Electrical Commissioning	May 10 th	May 24 th
\$14	Night Shift Electrical Commissioning	May 5 th	May 19 th
\$34	Night Shift Electrical Commissioning	May 4 th	May 18 th

Legend

- Turbine Locations
- Existing Public Road
- Project Access Road
- Waterbodies
- Trenching
- Aggregate Delivery
- Concrete Delivery
- Component Delivery
- Area of Potential
- Traffic Interruption
- Single Lane Restrictions
- Road Closures
- Detours
- Foundation Preparation and Curing
- Electrical Commissioning



0 750 1,500 Meters

PENNECON LIMITED

AMHERST ISLAND WIND PROJECT

Weekly Project Activity Map

DRAWING No. AMHST - 287 DATUM/PROJECTION: NAD83/UTM 18N
